


AVDASI2
 Network Diagrams
Activity-on-Arrow cheat sheet

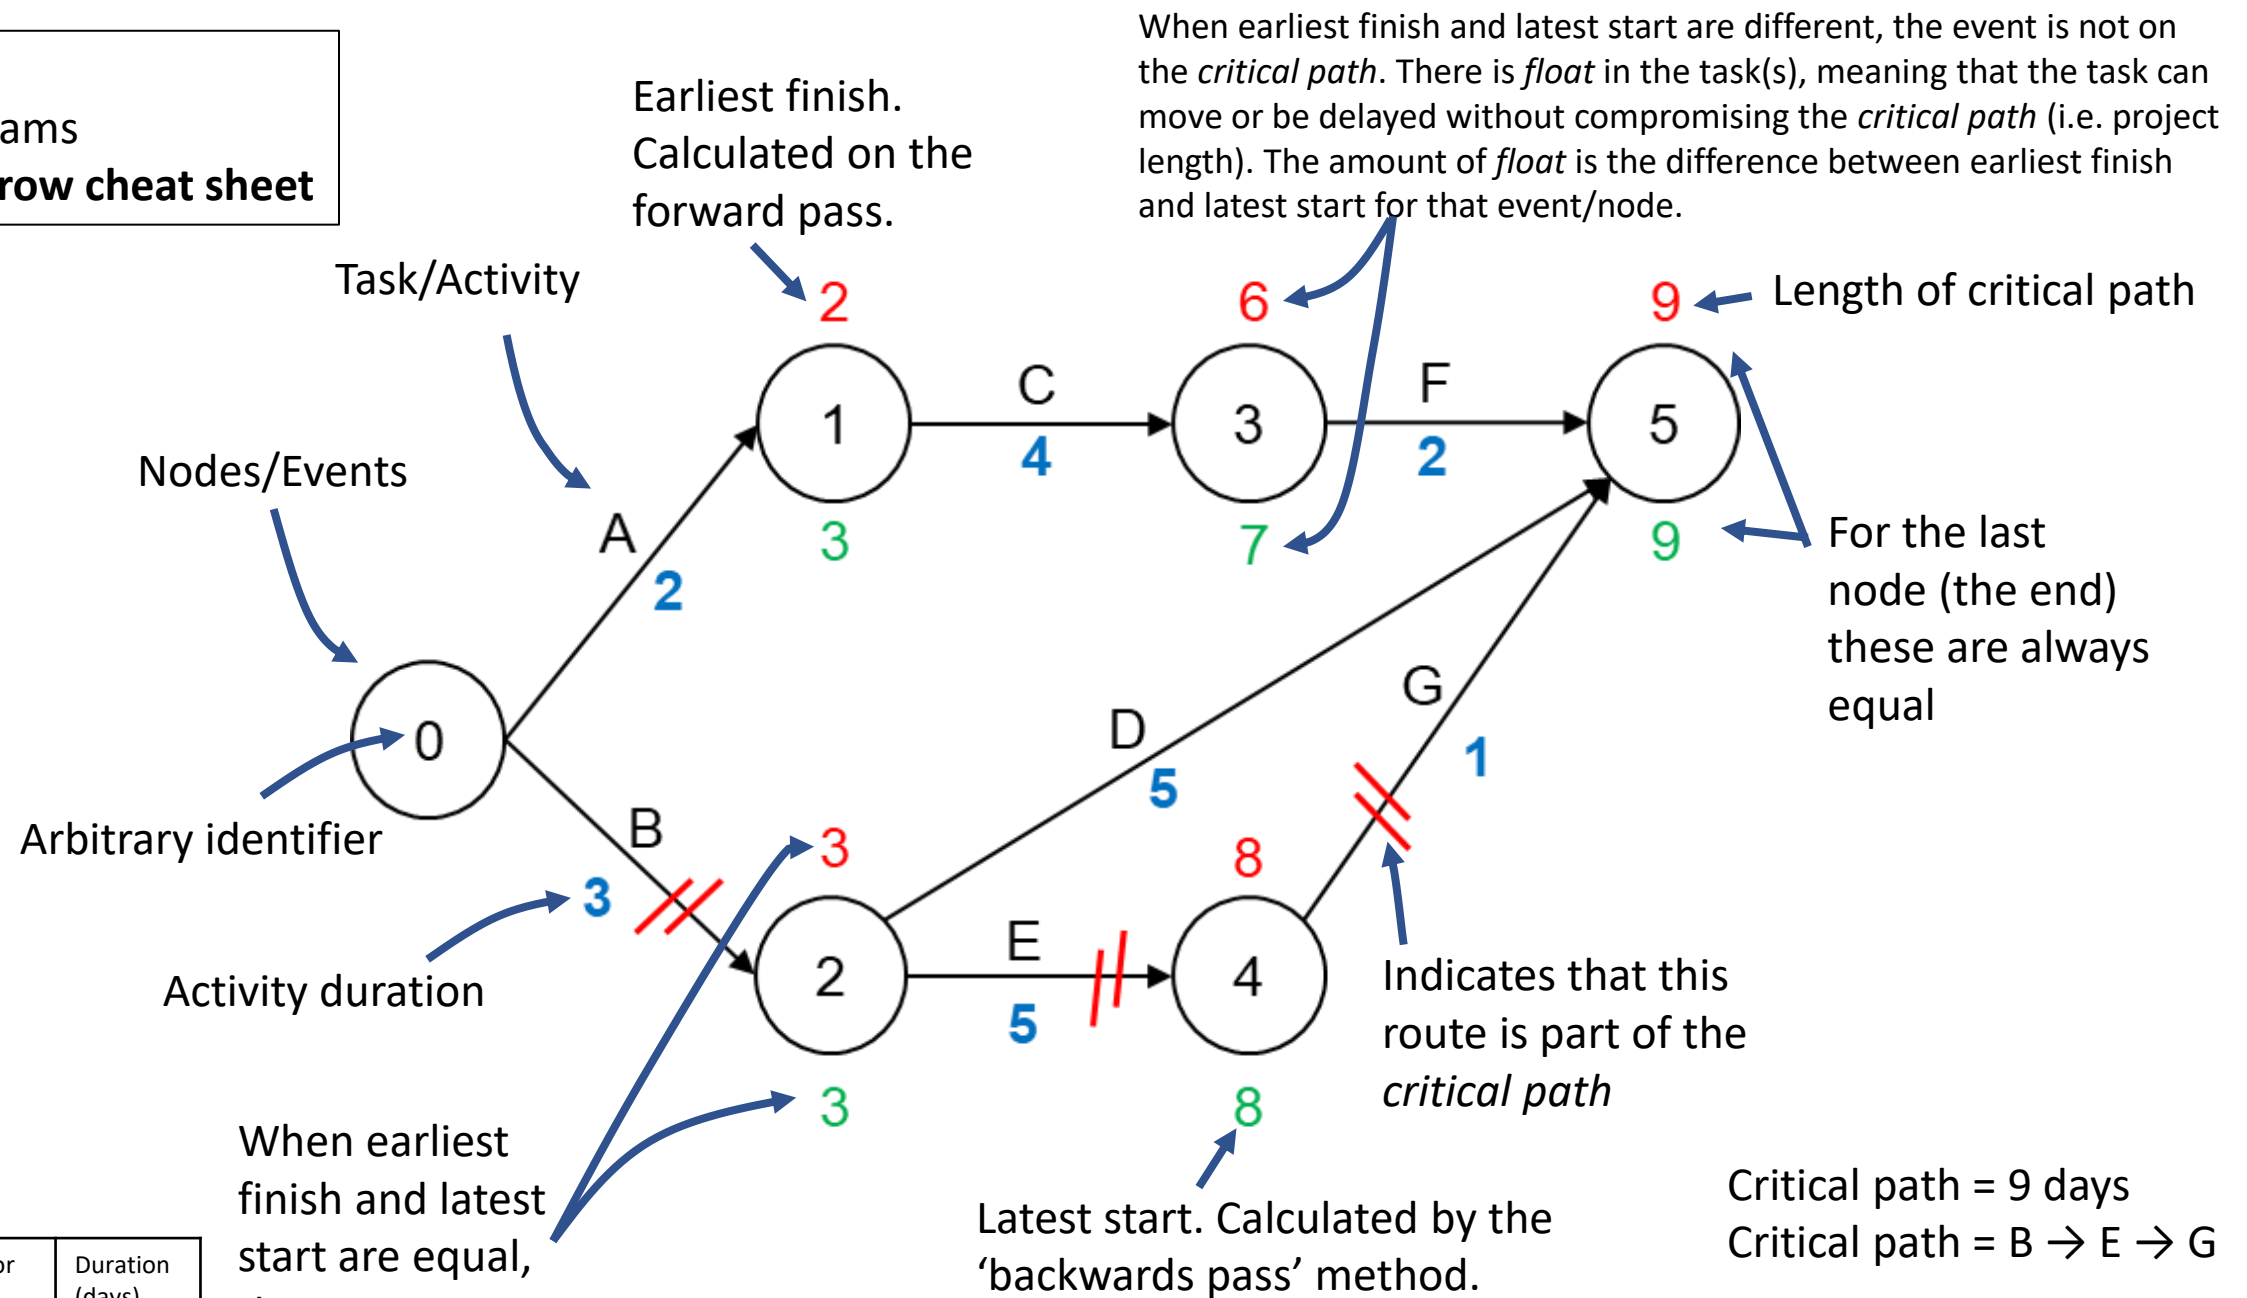

Activity	Predecessor	Duration (days)
A	(Start)	2
B	(Start)	3
C	A	4
D	B	5
E	B	5
F	C	2
G	E	1

Method

- Create a WBS to breakdown the project into tasks
- Consider the task dependencies and estimate the task durations
- Create a dependencies table (or use the network to explore the dependencies)
- Draw an activity-on-arrow network diagram
 1. Label the durations (next to the activity letter)
 2. Conduct the forward pass (identify earliest possible time at each node)
 3. Conduct the backwards path (subtract the task durations from the latest start times)
 4. State the critical path length
 5. Label the critical path routes. These are where the earliest and latest start times are equal.
 6. Identify any float i.e. which task(s) can be delayed (and by how much) without delaying the project end date?
